


EITS SUPPLIER FORUM

17TH MARCH 2023



EACOP PROJECT DESCRIPTION- SCHEMATIC

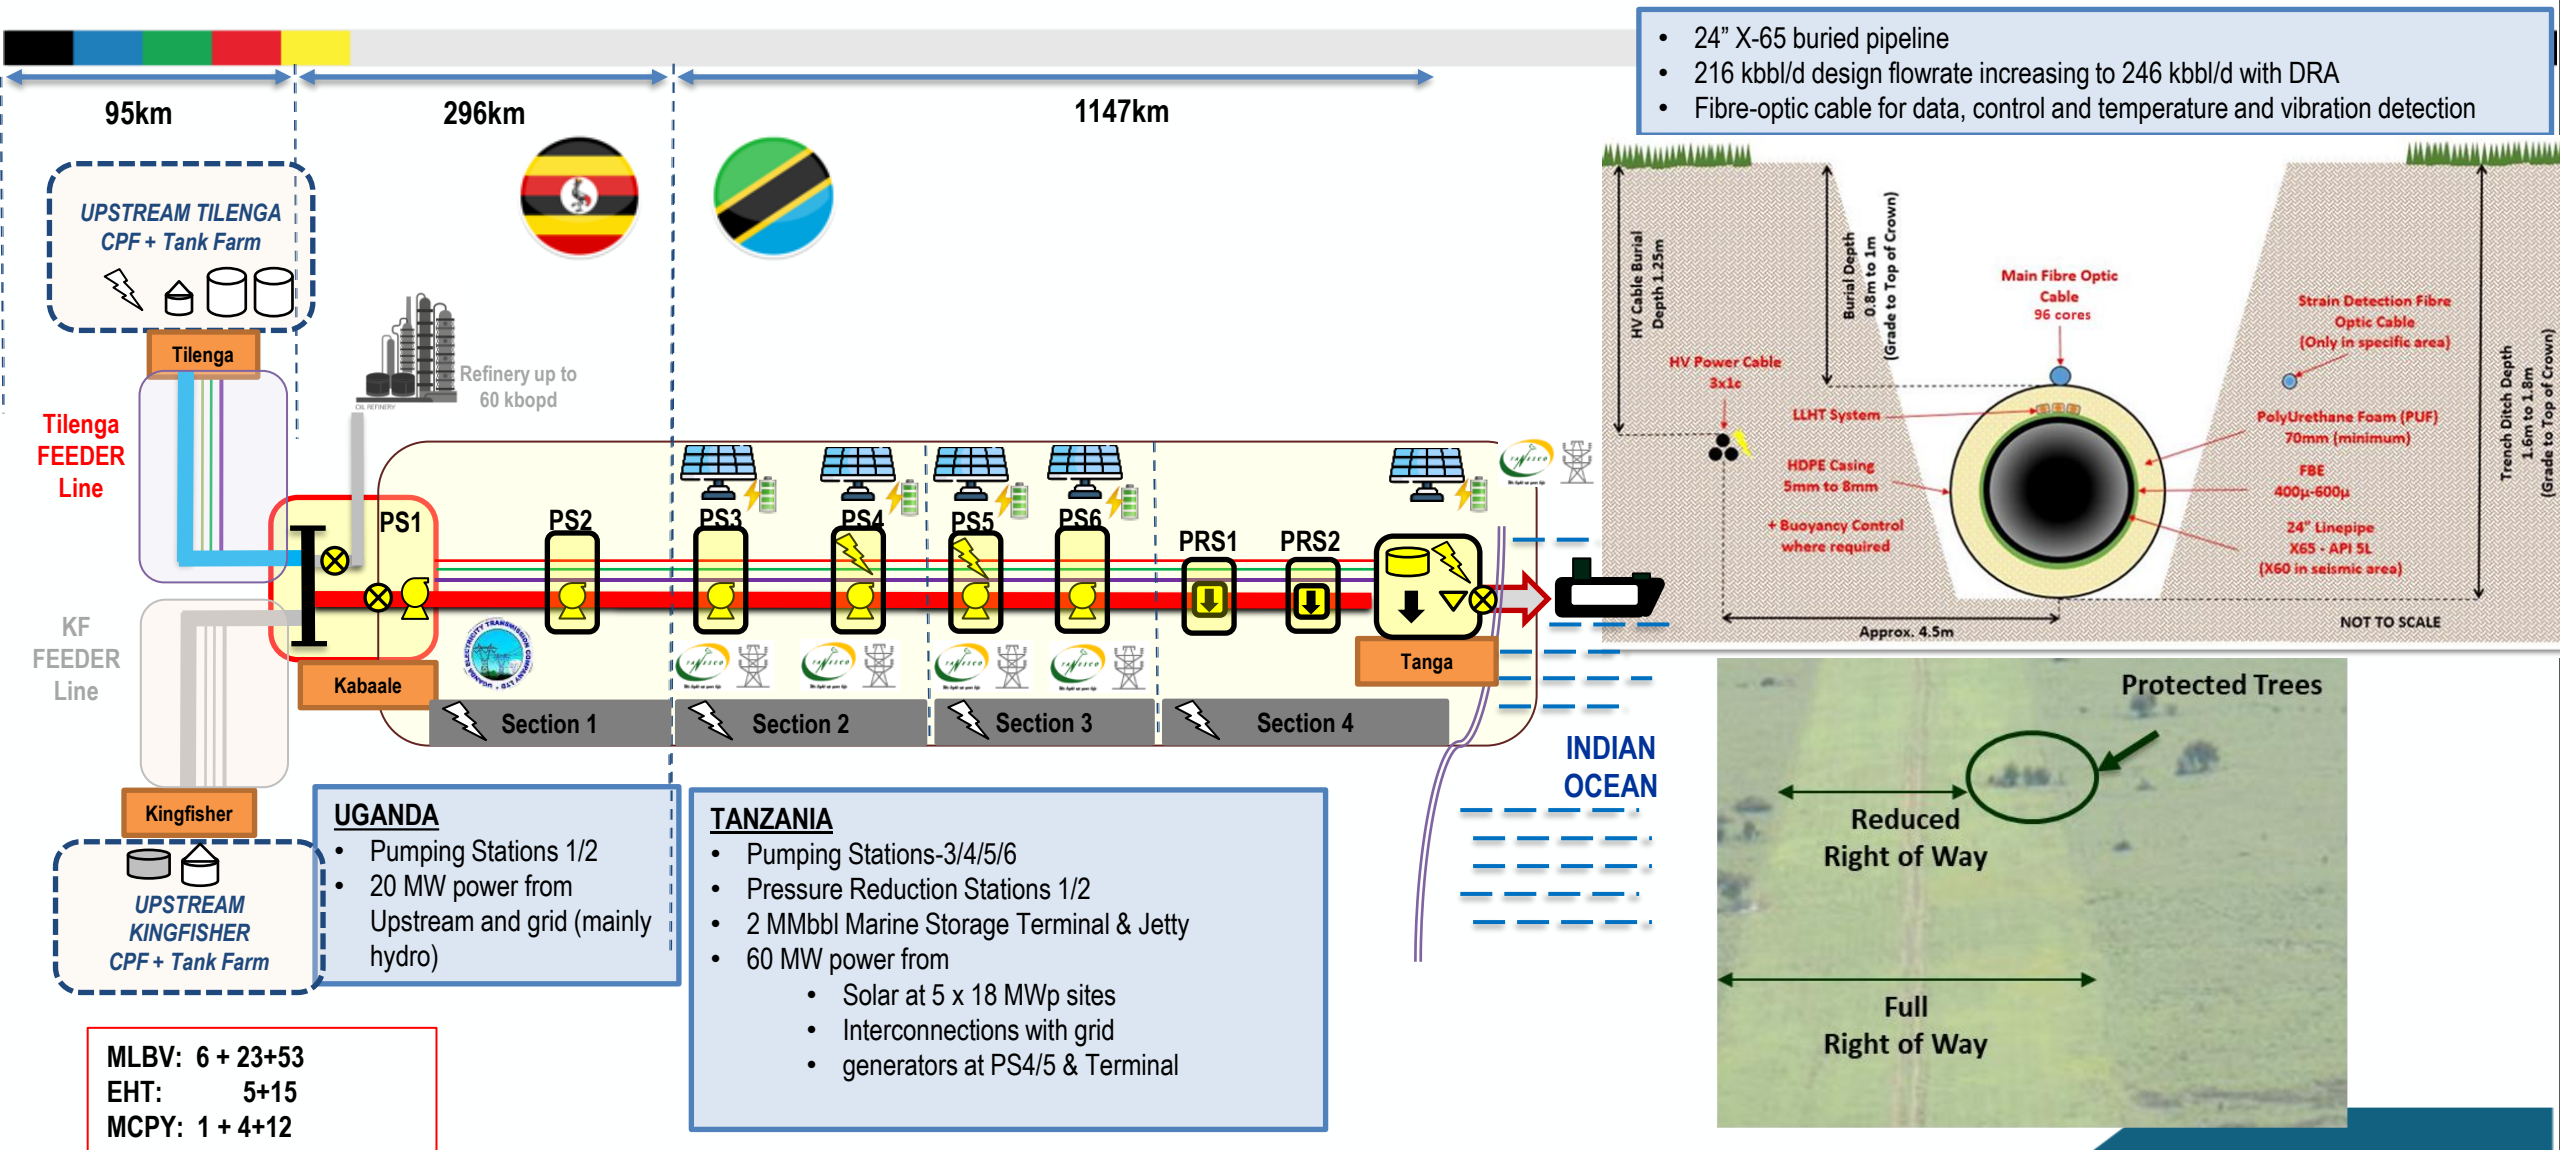

EACOP MAIN CONTRACTS

EACOP

Engineering & Procurement & construction management – **WORLEY (*) 24/2/22**

- **LINE-PIPES (*)**
CFT ongoing
- **THERMAL INSULATION (*)**
ISOAF JV 18/2/22
- **EITS (*)**
(Electrical, Instrumentation Control
Telecom Security)
SCHNEIDER/SNEF 18/2/22
- **LOGISTICS (*)**
BOLLORE 18/2/22
- **EACOP LLI**
Export Pumps 4/3/22
Power Gen 27/4/22
MLBV (*) 28/4/22
Electric Cables (*) 24/6/22

Early Civil Works (# yards / sites, all access roads, water wells)

RESERVED CONTRACTS in Uganda & Tanzania

Tz Lot 2 Milemba signed 15/10/21
Tz Lot 1 Nyanza signed 27/4/22
Water Sourcing Tz
Water Sourcing Ug
Tz Lot 3 JV SPEK signed 3/6/2022

Above Ground Infrastructures Construction

UG + TZ : 6x PS + 2x PRS

Pipeline Construction

Uganda -391 km & Tanzania -1147 km

CPP (China) – CLOA valid until 15/4/23

TERMINAL – **DAQING 3/5/22**


TANKS (EPC) – **DAQING 3/5/22**



JETTY (EPC) – **BBJV 1/6/2022**

2 contracts not yet awarded:

- Line pipe supply – scheduled March/April 2023
- Agi/Pipeline construction – scheduled for March/April 2023

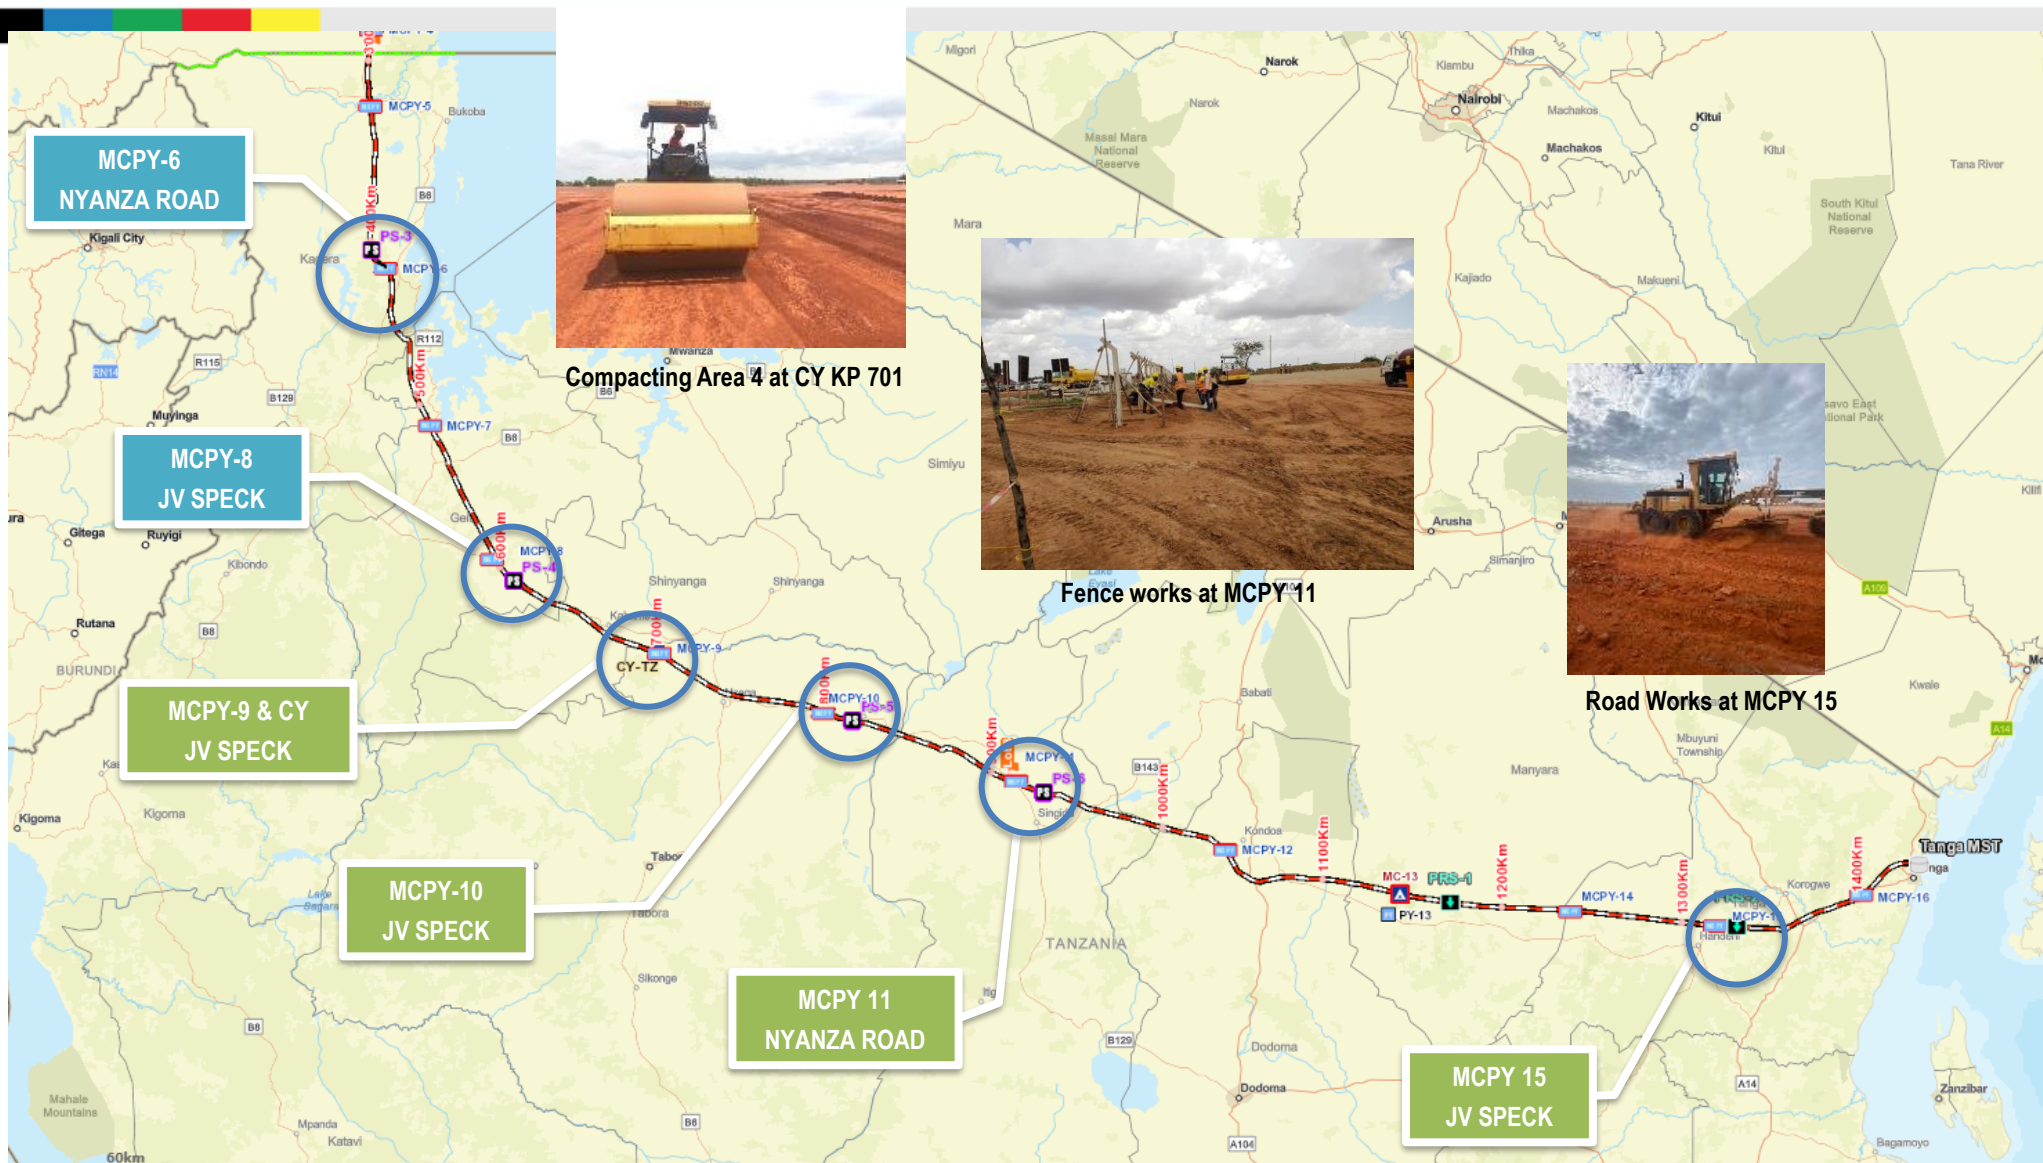ONGOING AND PLANNED EARLY CIVIL WORKS



-  **ON GOING ACTIVITIES**
-  **ACTIVITIES TO COMMENCE**



Current Status :

- Only geotechnical investigations on going (PS2 Access road, then PS1 and PS2)

Upcoming Early Civil Works:

- **PS 1 MC**
Activities to start in the coming 3 Months
Environmental assessment submitted to NEMA
- **MCPY 3 .**
Activities to start in the coming 3 Months

WATER SOURCING WORKS IN TANZANIA/ UGANDA

Uganda

- PS1 /2 in Uganda with ICS/ Newplan
- PS1/PS2 Access roads with ICS

Tanzania

- PS3 to PS6, PRS 1 & 2 in Tanzania with NORPLAN
- HDD River crossing location in Tanzania (Sigi river than Kagera) with CPP



PS 5: Drilling BHS - 06



Sigi River – Geotechnical team

COATING PLANT – CONSTRUCTION PROGRESS


Structural workshop erection started Nov 2022, current progress : **52%**



Satellite image - Coating Yard



Concrete slab ongoing @

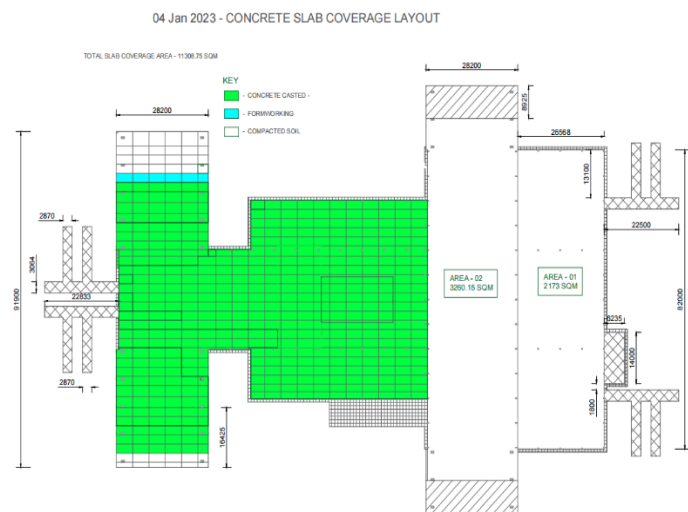

Status of Slab @ Coating Yard



Steel Structures Erection ongoing @
Coating Yard

Ready For operation: June/July 2023



Slab Concrete Casting ongoing @ Coating Yard



JETTY

- Land clearing / temporary site fence and rainwater drainage completed
- Top soil removal 60% (out of 400k m3 to be moved)
- Cut/fill \approx 20% (out of 300k m3 to be moved)

- Site Preparation 80% done
- Temporary Facilities/Camp commissioned
- Foundations to be started in June

Vision

- Promote economic development and national industrialization.
- Implementing an industrial development plan
- Capitalize on the development phase to build the capacity of the local companies and Ugandan Citizen
- Drive the growth of the Ugandan Oil & Gas Industry in line with the objective of Uganda for long term industrial development





Local Content Pillars

1. Employment & training
2. Goods & services
3. Capacity building & technology transfer



EITS SCOPE

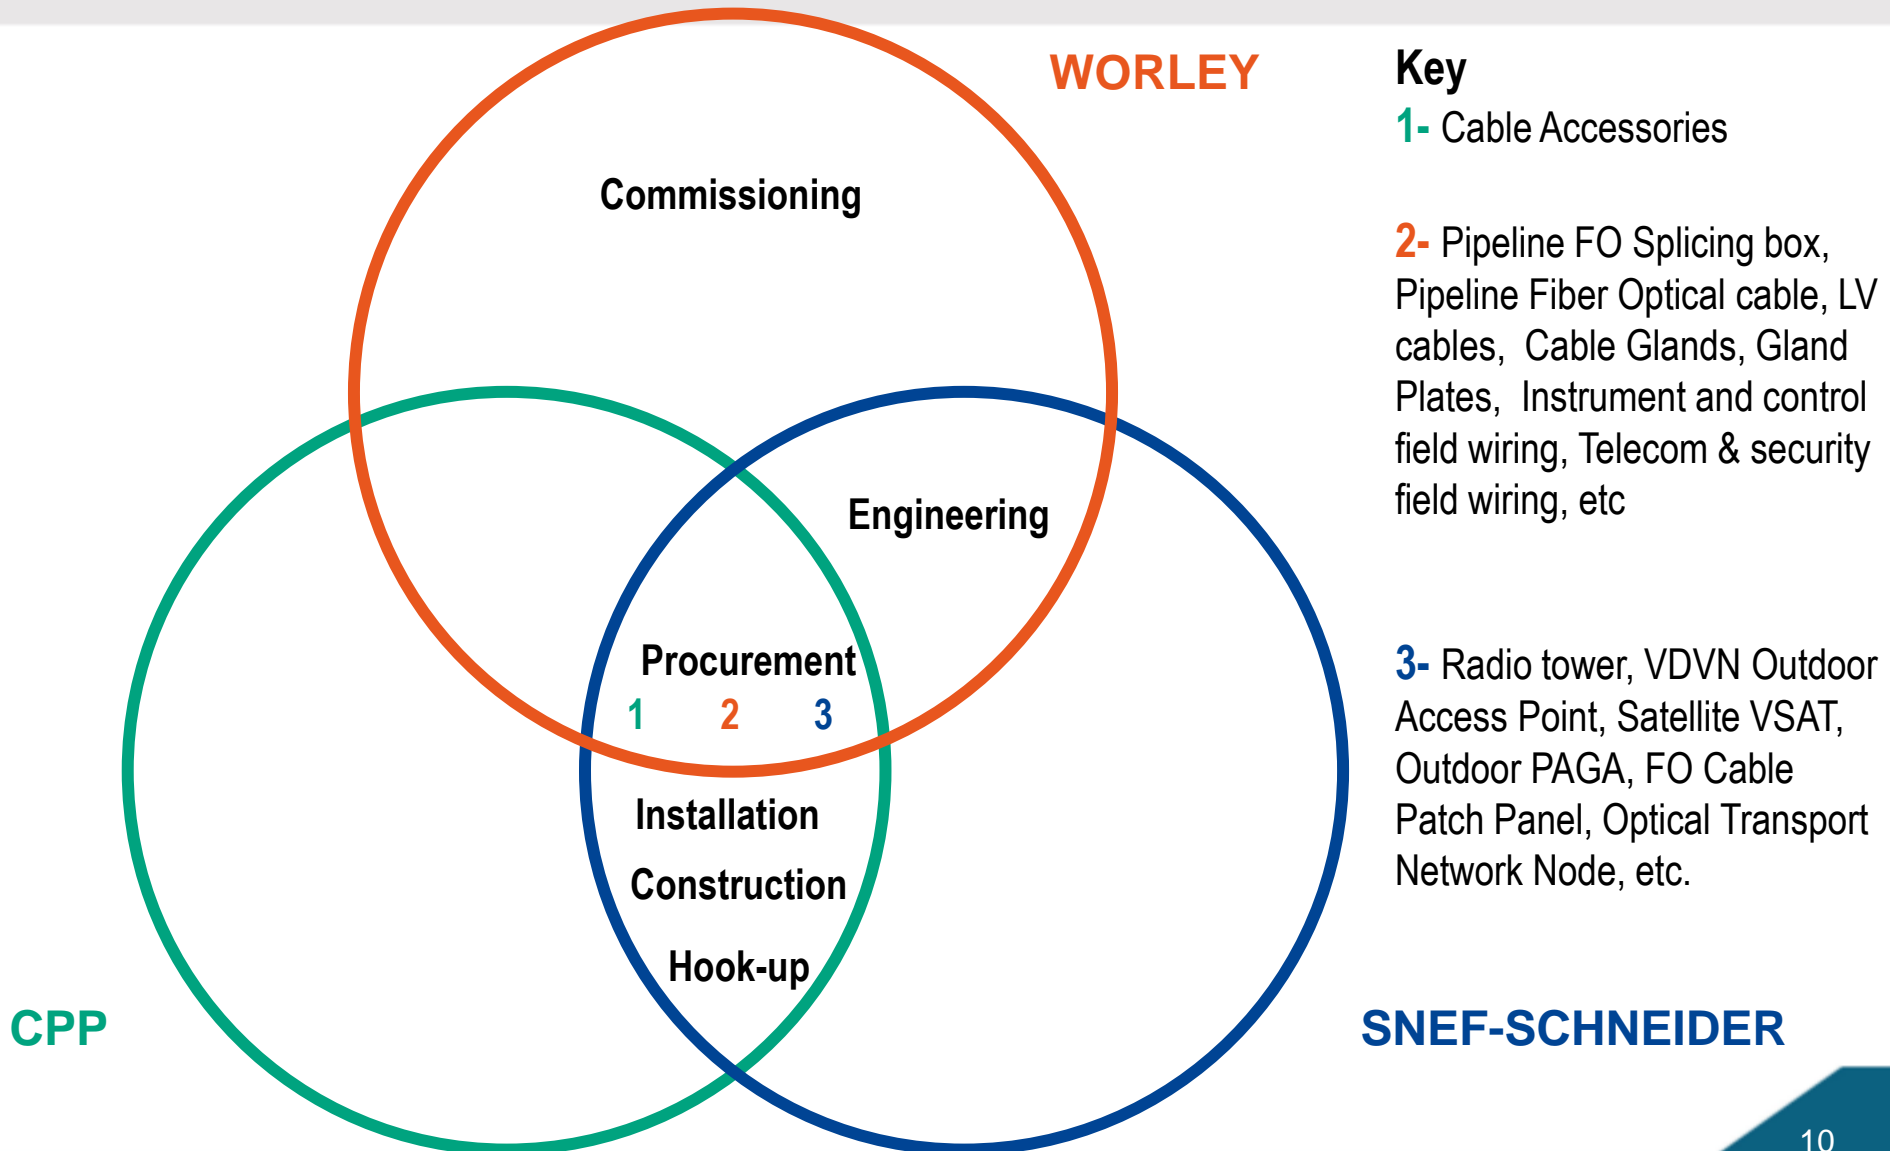

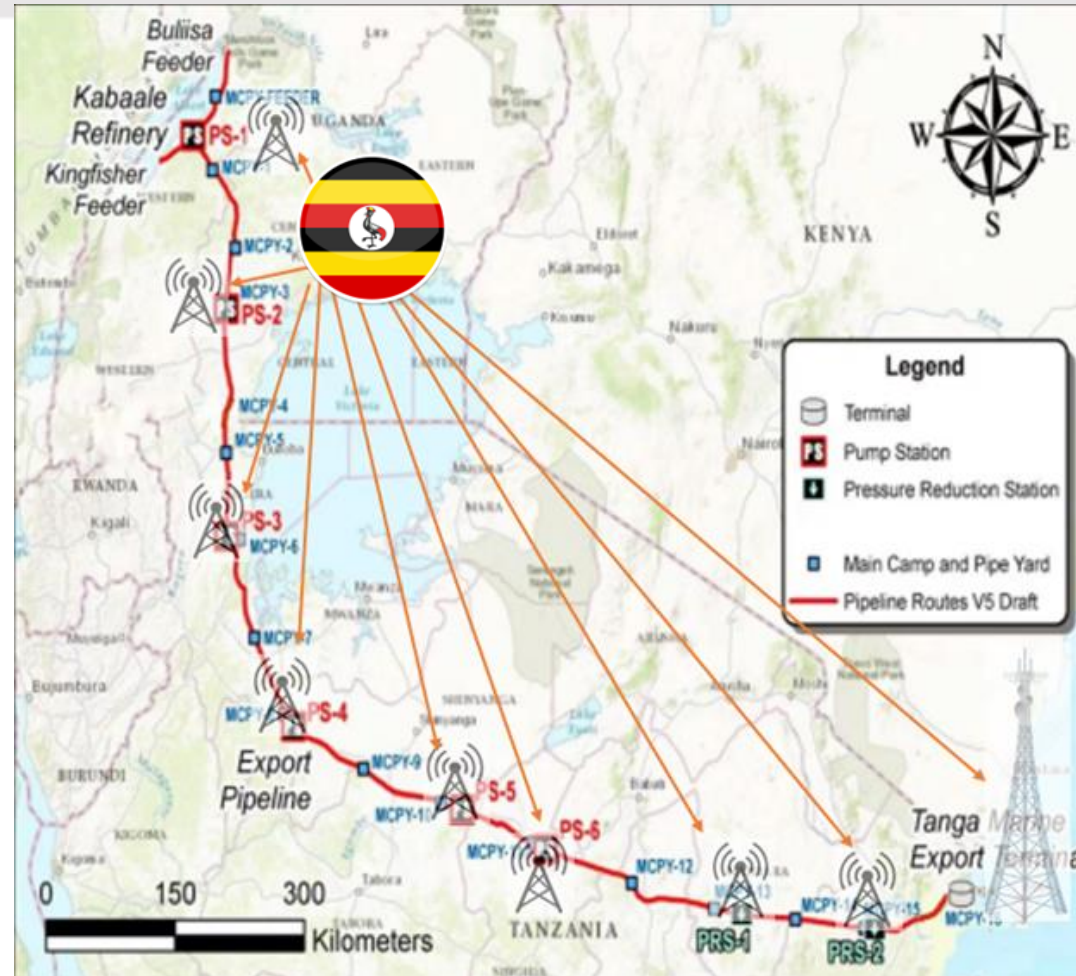

Note: All telecom and CCTV Masts (~300 in number) to be used across the project in both Tanzania and Uganda will be fabricated in Uganda

PURPOSE OF TODAY'S FORUM



Provide sector specific information on available opportunities on EACOP project



Answer your Questions



Provide an opportunity for networking with Tier 1 contractors

ANY QUESTIONS?



ASANTE
WEBALE
THANK YOU
MERCI
謝謝
